

EL PASO COUNTY DEPARTMENT OF HEALTH AND ENVIRONMENT  
INDIVIDUAL SEWAGE DISPOSAL SYSTEM INSPECTION FORM

Permit # 010621  
Date 10/21/96

9

APPROVED: YES ☒ NO ☐

#3132003010

ENVIRONMENTALIST Larry Schmid

Address 14550 TRIGGER RD Owner Beth & Carole Gregolein

Legal Description 00 Lot 29, Dayton Ranches

Residence ☒, # of bedrooms 4; Commercial ☐; System Installer RJR D. Lehn

SEPTIC TANK:

Commercial ☒; Noncommercial ☐; L       , W       , WD         
Construction Material Precast concrete, capacity 1500 gallons.

DISPOSAL FIELD:

Rock Systems:

Trench: depth       , width       , total length       , sq. feet       

Bed: depth       , length       , width       , sq. feet       

Rock type       , depth       , under PVC       , over PVC       

Seepage Pits: # of pits       , total # of rings       , working depth(s)         
size of pit(s) L X W       , lining material       , total sq. feet       

Rockless Systems:

Chamber: Type infiltrator, number of chambers 34, bed       , trench ☒  
sq. ft./section 18, reduction allowed 50 %, sq. ft. required 764  
total sq. ft. installed 1224, depth of installation 16-33"

Engineer Design Y or (N), Designing Engineer       


Approval letter provided? Y or N

Well 50 feet from tank (Y) or N 100 feet from leach field (Y) or N

Well installed at time of septic system inspection (Y) or N Public Water       

\*Approval will be revoked if in the future the well is found to be within 50 feet of the septic tank and/or 100 feet of the disposal field.

NOTES: Pipes SDR 35

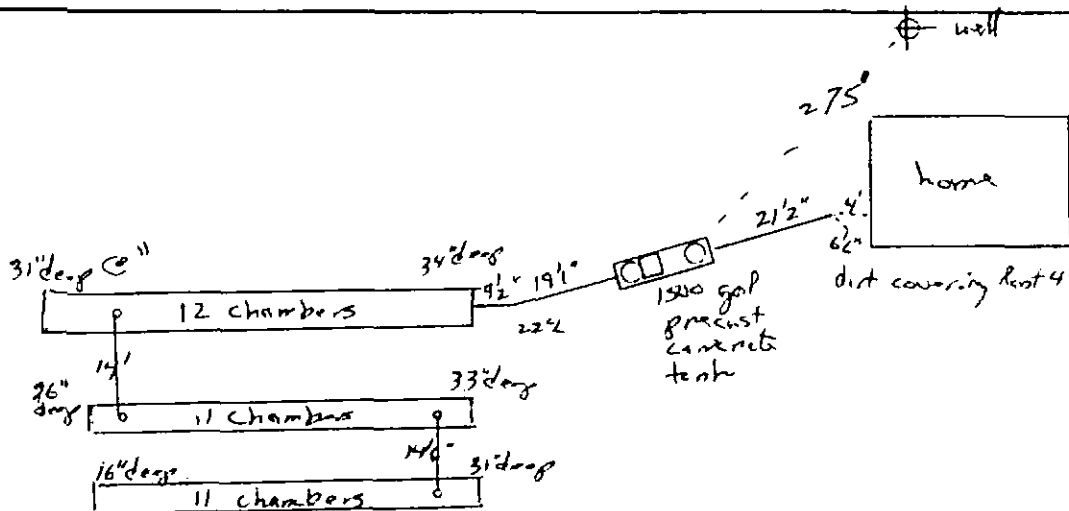

Trigger

Murphy

Acres 11 1/2 EL PASO COUNTY • DEPARTMENT OF HEALTH AND ENVIRONMENT

Water Supply WELL 301 South Union Blvd. • Colorado Springs, Colorado • 578-3125

Permit 010621

# PERMIT

TO CONSTRUCT, ALTER, REPAIR OR MODIFY ANY INDIVIDUAL SEWAGE DISPOSAL SYSTEM

Receipt No. ym

Issued to BETH & CAROLE GREGELEIN

Date 9-20-96

Address of Property 15000 MURPHY ROAD, LOT 31, PEYTON RANCHES

Phone 598-5560

14550 Trigger Rd (Permit valid at this address only)  
Sewage-Disposal System work to be performed by R & R DITCHING

Phone 338-9999

This Permit is issued in accordance with 25-10-106 Colorado Revised Statutes 1973, as amended. PERMIT EXPIRES upon completion-installation of sewage disposal system or at the end of twelve (12) months from date of issue-whichever occurs first-(unless work is in progress). This permit is revokable if all stated requirements are not met.

**-THIS PERMIT DOES NOT DENOTE APPROVAL OF ZONING AND ACREAGE REQUIREMENTS-**

**\$150.00**

PERMIT FEE (NOT REFUNDABLE)

**9-20-97**

DATE OF EXPIRATION

[Signature]  
DIRECTOR, DEPARTMENT OF HEALTH AND ENVIRONMENT  
[Signature]  
ENVIRONMENTALIST

NOTE: LEAVE ENTIRE SEWAGE DISPOSAL SYSTEM UNCOVERED FOR FINAL INSPECTION. 48 HOUR ADVANCE NOTICE REQUIRED.

SEPTIC TANK:	TRENCH SYSTEM:	BED SYSTEM:	SEEPAGE PIT SYSTEM:
1500	total square feet <u>764</u>		total square feet _____
_____ gallons	_____ ft. of trench _____ inches wide		
	_____ ft. of trench _____ inches wide	total square feet _____	_____ rings or _____ diam.x _____ w/d

NOTES: Groundwater at 7 feet; therefore, no part of level leach field can be deeper than 3 feet below ground surface. Install leach field in area of perc. test, but NO deeper than 36 inches. Recommend an increase of 60 per cent in leach field area (to 1222 sq. ft.)(no NOT taking the reduction if chambers are used) because of the clothes washer & garbage disposal.

The Health Office shall assume no responsibility in case of failure or inadequacy of a sewage-disposal system, beyond consulting in good faith with the property owner or representative. Free access to the property shall be authorized at reasonable time for the purpose of making such inspections as are necessary to determine compliance with requirements of this law.

ION  
Roy Palsen  
495-4710

OWNER'S SIGNATURE Carol Gregelem Date 28 Aug 96

764 ft<sup>2</sup> 1500 gal 9/9/96

Absorption Area Tank Capacity Date of Site Inspection

REMARKS: Groundwater at 2 ft; therefore no part of leach field can be deeper than 3 ft below ground surface. Install leach field in area of perc test, but no deeper than 36". Recommend an increase of 60% in leach field area (to 1222 ft<sup>2</sup>) or NOT taking the reduction of chambers are used) because of the clothes washer and garbage disposal being installed in the home.

EHS INSPECTOR Larry School Date 9/9/96

PERMIT # 10621 FEE NO FEE DATE TO EPC PLANNING DEPT 8/27/96

We require the ORIGINAL of your percolation (PERC) TEST.

The following information must be on your PLOT PLAN.

Property lines

Proposed septic system site

Well(s)

Building(s)

Water line

Subsoil drain(s)

Property dimensions

Designated alternate septic system site

Adjacent property well(s)

Proposed building(s)

Cistern

If any of these are within 100 feet of your proposed septic system  
include on your plot plan

Spring(s)

Pond(s)

Dry Gulch(s)

Lake(s)

Stream(s)

Natural drainage course(s)

PROPERTY AND PERC HOLES MUST BE CLEARLY MARKED OR POSTED

GIVE COMPLETE DIRECTIONS TO THE PROPERTY FROM A MAIN HIGHWAY

