

#5304002005

Black Forest

5 acres/well con

2322

file

CITY-COUNTY HEALTH DEPARTMENT
COLORADO SPRINGS, COLORADO

SEWAGE DISPOSAL INSPECTION FORM

APPROVAL: V.A. & F.H.A.
YES ☒ NO ☐DATE OF INSP. 1 Aug. 73
ENVIRONMENTALIST E. HanksLOCATION (STREET NUMBER) 8185 Mustang Rd. OCCUPANT Robert EvansLEGAL DESCRIPTION Lot #3, Filing #2, Pawnee Rancheros 473-1373 Ext. 43CONTRACTOR _____ NO. OF BEDROOMS 3 bdrms.TYPE OF CONSTRUCTION HouseSYSTEM INSTALLED BY Merrill Excavation

PRIMARY TREATMENT

COMMERCIAL MFG. Pre-cast S.T. SIZE 1250 gals.

NON. COMMERCIAL _____ SIZE _____

TYPE OF MATERIAL _____ NO. COMPARTMENTS _____

WIDTH _____ LENGTH _____ GALLONS _____ DEPTH (TOTAL) _____ LIQ. CAP. _____


SECONDARY TREATMENT

DISPOSAL FIELD Leach lines SOIL silt-sand PERC. TEST 3 min./in.TOTAL LENGTH OF TILE LINES 109' NUMBER OF LINES two DISTANCE BETWEEN LINES 10-14'ABSORB. AREA 327^{sq} TYPE OF TILE Orange TRENCH DEPTH 3' TRENCH WIDTH 3' GRADE slightTYPE FILTER MATERIAL 2" rock DEPTH 12" UNDER TILE 6" OVER TILE 2"

LEACHING PITS (NO.) _____ SOIL _____ PERC. TEST _____ LINING MATERIAL _____

CAPACITY SQ. FT. _____ DIAM _____ WORKING DEPTH _____

DISPOSAL BED LENGTH _____ WIDTH _____ DEPTH _____ TOTAL SQ. FT. _____

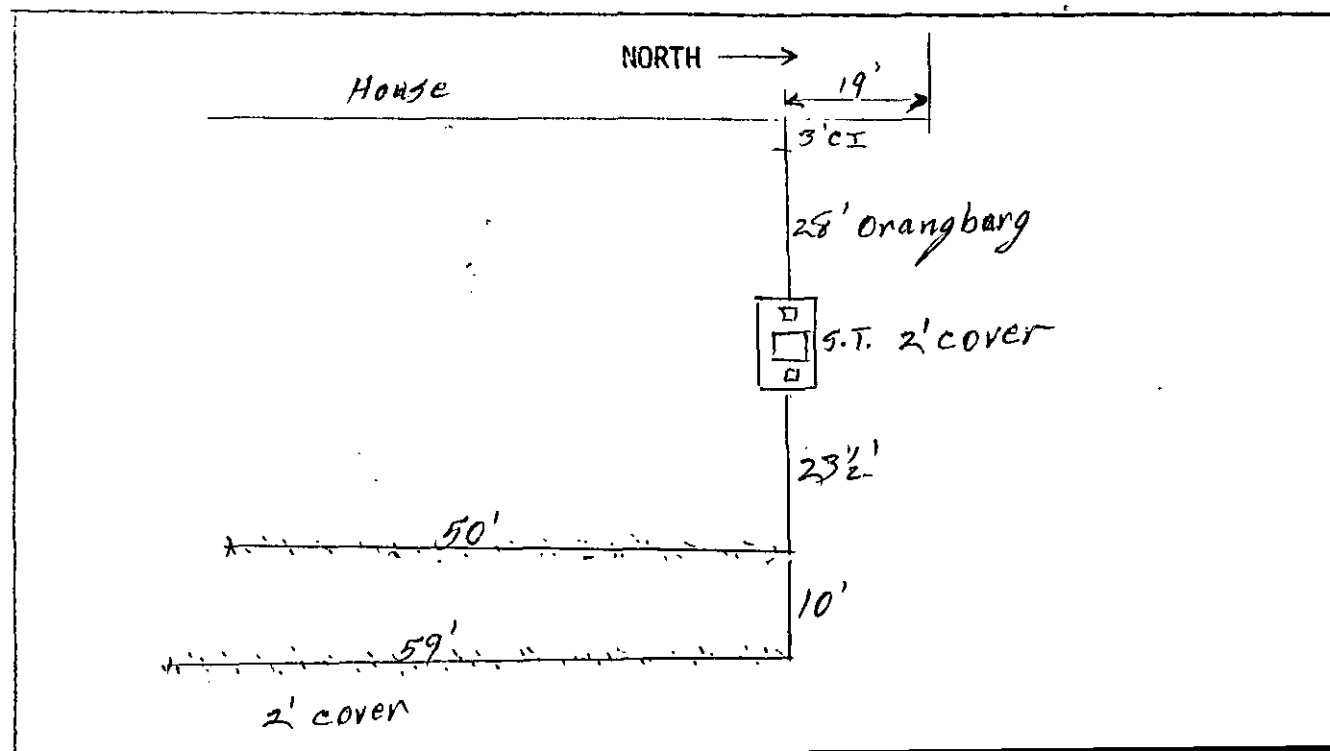

Acres 5EL PASO COUNTY CITY-COUNTY HEALTH DEPARTMENT
501 North Foote Avenue Colorado Springs, Colorado 471-3700

No. 02322

Water Supply well

PERMIT

Receipt No. _____

TO CONSTRUCT, ALTER, REPAIR OR MODIFY AN INDIVIDUAL SEWAGE DISPOSAL SYSTEM

Issued To Merrill ExcavationDate May 1 1973Address of Property Lot #3 Filing #2 Pawnee Rancheros

(Permit valid at this address only)

Builder - Contractor - Owner Address _____

Phone 749 2505

Sewage-Disposal System work to be performed by _____

Phone _____

This Permit is issued in accordance with Regulation XII and Article 2 of Chapter 66, Colorado Revised Statutes, 1963, as amended by the addition of a new Section 66-2-16. (H.B. 1205, 7-1-65). PERMIT EXPIRES upon completion of installation of sewage disposal system or at the end of six (6) months from date of issue - whichever occurs first - (unless work is in progress):

This Permit does not denote approval of zoning and other requirements.

Permit Fee \$25.00

Director, City-County Health Department

Date of Expiration Nov 1 1973Environmentalist W. H. Richard

NOTE: LEAVE ENTIRE SEWAGE DISPOSAL SYSTEM UNCOVERED FOR FINAL INSPECTION.

24-HOUR ADVANCE NOTICE REQUIRED

Septic tank 1000 gals. Field 100 Feet of trench 36 inches wide

OR Field _____ Feet of trench _____ inches wide

Seepage bed _____ ft. long _____ ft. wide. Seepage pit _____ sq. ft. _____ diam. _____ w/d

The Health Officer shall assume no responsibility in case of failure or inadequacy of a sewage disposal system, beyond consulting in good faith with the property owner or representative. Free access to the property shall be authorized at reasonable times for the purpose of making such inspections as are necessary to determine compliance with requirements of this regulation.

DARLOW ENGINEERING CO.
12635 HOLMES RD.
COLO. SPGS., COLO. 80908
495-2853

#5304002009
08/01/1973
8185 MUSTANG RD


PERCULATION TEST REPORT

Test Hole: 8 in. dia. X 36 in. depth

Water Level: -10'4

Test Results: - 3 - minutes per 1 inch

Range of each Layer ↓		Top Soil	Clay	Silt	Fine Sand	Course Sand	Gravel	Course Gravel	Other
1st	<u>4"</u>	✓							
2nd	<u>5"-14"</u>		<u>Trace</u>		✓	✓	<u>Loose</u>		
3rd	<u>15"-36"</u>		"	✓	✓		<u>Semi Loose</u>		
4th									
Indicate Packed or Loose ◇									



Henry W. Danley, P.E.
Structural Engineer

Henry W. Danley

Test performed for BOB EVANS
Address _____

Location of Test LOT #3 FILING #2
PANNER RANCHERO'S
EL PASO COUNTY
Date APRIL 26, 1973

This form must be accompanied by a plot plan (rough Sketch).

The lengths of the property lines, the position of the house relative to the property lines, the general location of the well and the septic tank and the distance from the leech field to the well (100 feet plus) must be on the sketch.
