

Columbine Estates
P

EL PASO COUNTY HEALTH DEPARTMENT
COLORADO SPRINGS, COLORADO

SEWAGE DISPOSAL INSPECTION FORM

6309010007

File # 596
DATE 9/26/77 # 4754

APPROVAL: YES NO

ENVIRONMENTALIST John M. Dunham

LOCATION (street number) 2235 SHRIDER RD COMPANY A. RABOENY

LEGAL DESCRIPTION Lot 1, Blk 3, Columbine Estates

TYPE OF CONSTRUCTION FRAME NO. OF BEDROOMS 4

SYSTEM INSTALLED BY SAME

COMMERCIAL MFG. El Paso SIZE 1250 GAL.

TYPE OF MATERIAL conc. NO. COMPARTMENTS 2


WIDTH _____ LENGTH _____ DEPTH (total) _____ LIQ. CAP. _____

DISPOSAL FIELD: BED OR TRENCH DEPTH SEE BELOW WIDTH 12' LENGTH 79' SQ. FT. 948

DISTANCE BETWEEN LINES _____ ROCK _____ DEPTH _____ UNDER _____ OVER _____

LEACHING PITS (NO.) _____ LINING MATERIAL _____ CAPACITY SQ. FT. _____

SEE ATTACHED DRAWING

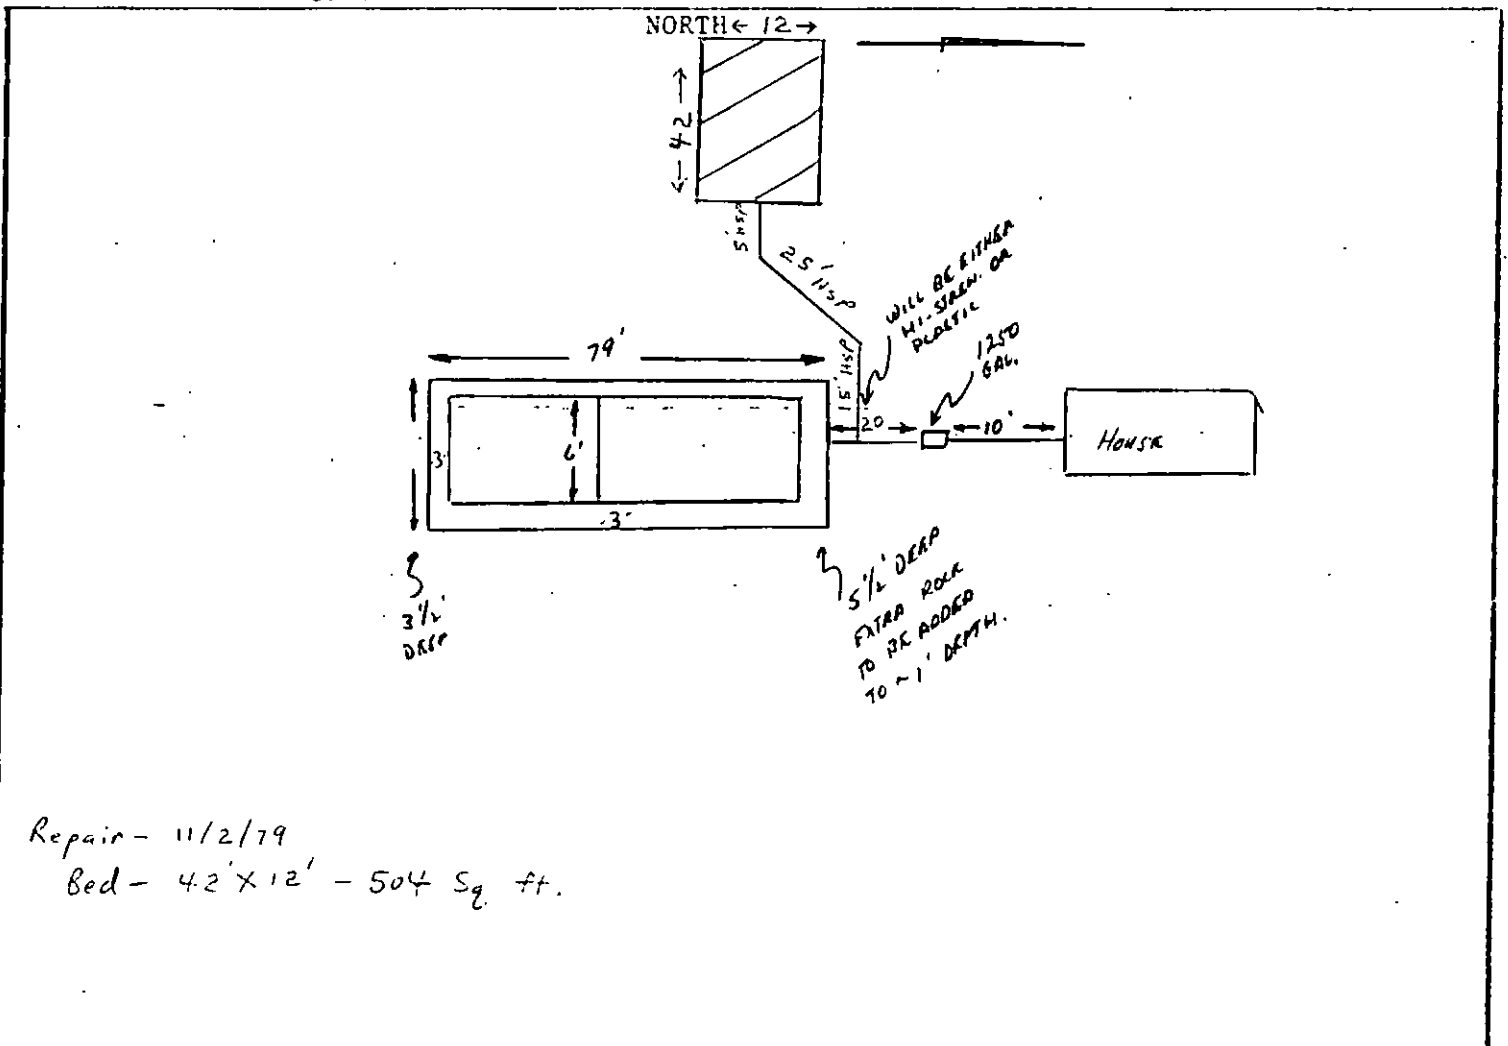

Repair - 11/2/79
Bed - 42' x 12' - 504 Sq. ft.

Acres 1

EL PASO COUNTY . CITY-COUNTY HEALTH DEPARTMENT.
501 North Foote Avenue . Colorado Springs, Colorado - 475-8240

04754

Water Supply Well

Receipt No. 02

PERMIT

TO CONSTRUCT, ALTER, REPAIR OR MODIFY AN INDIVIDUAL SEWAGE DISPOSAL SYSTEM

Issued To Alfred A. Rabideau Date April 21, 1977

Address of Property ~~7700 Stinson, Lot 1~~; Plot 3, Columbine Estates, C.S.
2235 Shmider Rd (Permit valid at this address only)

Builder - Contractor - Owner Address Same Phone _____

Sewage-Disposal System work to be performed by Same Phone _____

This Permit is issued in accordance with Regulation XII and Article 2 of Chapter 66, Colorado Revised Statutes 1963, as amended by the addition of a new Section 66-2-16. (H.B. 1205, 7-1-65). PERMIT EXPIRES upon completion-installation of sewage-disposal system or at the end of six (6) months from date of issue - whichever occurs first - (unless work is in progress).

- This Permit does not denote approval of zoning and acreage requirements. -

Charles M. Dowding, Jr., M.D., M.P.H.

Permit Fee October 21, 1977 \$50.00

Director, City-County Health Department
Robert S. Harris
Environmentalist
John Von der Haan

Date of Expiration

NOTE: LEAVE ENTIRE SEWAGE-DISPOSAL SYSTEM UNCOVERED FOR FINAL INSPECTION.

24-HOUR ADVANCE NOTICE REQUIRED

Septic tank	<u>1250</u> gals.	Field	<u>250</u>	Feet of trench	<u>29</u> inches wide
	OR-	Field	<u>167</u>	Feet of trench	<u>36</u> inches wide
Seepage bed	_____ ft. long	_____ ft. wide.	Seepage pit	_____ sq. ft.	_____ diam. _____ w/d

The Health Officer shall assume no responsibility in case of failure or inadequacy of a sewage-disposal system, beyond consulting in good faith with the property owner or representative. Free access to the property shall be authorized at reasonable times for the purpose of making such inspections as are necessary to determine compliance with requirements of this regulation.

EL PASO CITY-COUNTY HEALTH DEPARTMENT
501 NORTH FOOTE AVENUE
COLORADO SPRINGS, COLORADO
475-8240 EXT. 220

Application for permit to construct, Remodel, or Install a Sewage Disposal System

Name of Owner ALFRED A. RABIDEAU Phone 598-1856

Address of Property 7189 STINSON 2235 Sheridan Rd

Legal Description of Property LOT 1 PLOT 3 COLUMBINI ESTATES

Owner's Address (if different) 2935 EL CAPITAN Phone 598-1856

Systems Contractor OWNER Address _____

Type of Construction _____ Source and Type of Water Supply WELL

Size of Lot 343 FT X 343 FT

The construction of the Sewage Disposal System will comply with all applicable Laws, Ordinances, Standards or Resolutions.

HEALTH DEPARTMENT USE ONLY

Permit Number _____ Receipt Number _____

Number of Bedrooms 4 Tank Capacity 1250 gallons Absorption area 500 Sq. Ft.

REMARKS LOT LOOKS GOOD - GENTLE SLOPE - SANDY - ENOUGH ROOM TO

EXPAND. NEED PERC. TEST

APPLICATION IS APPROVED DENIED

ENVIRONMENTALIST [Signature] DATE 4/20/ 1977

PLOT PLAN WILL INCLUDE THE FOLLOWING

Plot plan may be drawn on the back of this sheet or on a separate sheet.

1. Streams, Lakes, Ponds, Irrigation Ditches and other Water Courses
2. North Direction
3. Location of Property Line
4. Buildings
5. Wells
6. Location of Proposed Septic System
7. Location of percolation test
8. Geographical features
9. Other Information as required

6309010007

09/26/1977

E

DARLOW ENGINEERING CO.
12635 HOLMES ROAD
COLORADO SPRINGS, COLORADO 80908

2235 SHRIDER RD

495-2853

PERCULATION TEST REPORT

3 TEST HOLES: 8 " DIA. X 30 " IN DEPTH

WATER LEVEL 8'±

RESULTS (MINS. / 1")

1 2 3 AVERAGE

5 5 5 5

8 FT. DEEP SOIL SAMPLE HOLE

RANGE OF EACH LAYER To 8 Feet	TOP SOIL	SAND	CLAY HARD	CLAY SOFT	PACKED or LOOSE	GRAVEL	SAND & GRAVEL	SILT	DECOMPOSED GRANITE	BED ROCK
0-6"	✓									
6"-8'		✓		TRAIL						

TIME AND DATE OF PRE-SOAK

9/20/77 9 AM

TIME AND DATE OF TEST

9/20/77 5:30 PM

TEST FOR


AL RABIDEAU
2935 EL CHARITAN
COLO. SPR. COLO
80918

LOCATION OF TEST

7189 STINSON
LOT #1 PLOT 3
OF COLUMBINE
ESTATES

THIS FORM MUST BE ACCOMPANIED BY A PLOT PLAN SHOWING THE LENGTHS OF THE PROPERTY LINES, THE POSITION OF THE BUILDING RELATIVE TO THE PROPERTY LINES, THE GENERAL LOCATION OF THE WELL AND THE SEPTIC TANK AND THE DISTANCE FROM THE LEECH FIELD TO THE WELL (MIN. 100 FEET)

HENRY W DANLEY P.E.



AL. RABIDEAU
 7189 STINSON DR. - CORNER OF SHRIEDER
 COLO. SPRINGS TEL. NO. 598-1856

